

EV27 dependency flow

Printed 2026-09-02 12:46 UTC · CSV: ev27_sample.csv (40 rows) · 12 sub-item rollups

40

WORK ITEMS

59

DEPENDENCIES

2

DATE CONFLICTS

20

BLOCKED

14

READY NOW

6

MODULES

○ Backlog

🕒 Ready

🔄 In Progress

⊗ Blocked

👁 Review

● Done

× Dropped

⚡ blocked

● ready now

⚡ dashed red = dependency loop

↪ thin arrow = sub-item rolling up to its parent

⚠ = blocker due after the thing it blocks

Blocked right now

Waiting on something that is not Done.

ID	WORK ITEM	STATE	NOW	WAITING ON	BLOCKS	OWNER	TARGET
EV27-25	Driveline assembly	○ Backlog	blocked	EV27-23, EV27-24	EV27-38	—	2027-01-09
EV27-10	Order HV fuse, contactors, IMD	🕒 Ready	blocked	EV27-7	—	Megan	2026-10-01
EV27-101	Tractive system — complete	○ Backlog	blocked	EV27-3, EV27-4, EV27-5, EV27-7, EV27-11	—	Aidan	2026-12-12
EV27-11	Tractive system indicator lights build	⊗ Blocked	blocked	EV27-6	EV27-101	—	2026-11-21
EV27-12	Shutdown loop bench test rig	○ Backlog	blocked	EV27-3, EV27-4	EV27-38	—	2026-12-05
EV27-9	Flex PCB cell sensing board rev A	⊗ Blocked	blocked	EV27-8, EV27-14	EV27-21	Aidan	2026-11-07
EV27-35	APEX telemetry board schematic (ESP32 + SX1262)	🕒 Ready	blocked	EV27-34	—	Aidan	2026-10-24
EV27-36	Optoisolated shutdown-loop telemetry taps	○ Backlog	blocked	EV27-34	EV27-38	—	2026-11-07
EV27-37	Wheel speed Hall sensor integration	○ Backlog	blocked	EV27-34, EV27-32	—	—	2026-11-14
EV27-38	Full vehicle wiring integration check	○ Backlog	blocked	EV27-12, EV27-21, EV27-25, EV27-36	—	—	2027-01-23
EV27-100	Accumulator — complete	○ Backlog	blocked	EV27-15, EV27-16, EV27-17, EV27-18, EV27-19, EV27-21	—	Aidan	2026-12-31
EV27-15	Accumulator container design	🔄 In Progress	blocked	EV27-14	EV27-17, EV27-26, EV27-100	Megan	2026-10-10
EV27-16	Segment layout and one-cell-failure redundancy	🔄 In Progress	blocked	EV27-14	EV27-18, EV27-19, EV27-100	Megan	2026-10-10
EV27-17	Accumulator thermal management study	🕒 Ready	blocked	EV27-15	EV27-100	—	2026-10-17
EV27-18	Cell interconnect method selection	🕒 Ready	blocked	EV27-16	EV27-21, EV27-100	Aidan	2026-10-17
EV27-19	Purchase order: Enepaq modules	○ Backlog	blocked	EV27-14, EV27-16	EV27-21, EV27-100	Megan	2027-02-01
EV27-21	Accumulator assembly and pack build	○ Backlog	blocked	EV27-19, EV27-18, EV27-9	EV27-38, EV27-100	—	2026-12-19
EV27-26	Accumulator mounting structure	○ Backlog	blocked	EV27-15	—	—	2026-11-07
EV27-27	Chassis nodes for HV routing	🕒 Ready	blocked	EV27-6	—	—	2026-10-24
EV27-33	Suspension pickup point revision	○ Backlog	blocked	EV27-31	—	—	2026-11-07

Ready to start


No unfinished upstream dependencies.

ID	WORK ITEM	STATE	NOW	WAITING ON	BLOCKS	OWNER	TARGET
EV27-23	Sprocket and chain procurement	🕒 Ready	ready	—	EV27-25	—	2026-10-10
EV27-24	Motor mount design	🔄 In Progress	ready	—	EV27-25	—	2026-10-17
EV27-3	Inertia switch requirements + spec doc	🔄 In Progress	ready	—	EV27-12, EV27-101	Aidan	2026-09-19
EV27-4	BSPD circuit design and validation plan	🔄 In Progress	ready	—	EV27-12, EV27-101	Megan	2026-09-26
EV27-5	APPS / BSE plausibility implementation	🕒 Ready	ready	—	EV27-101	Aidan	2026-10-03

ID	WORK ITEM	STATE	NOW	WAITING ON	BLOCKS	OWNER	TARGET
EV27-6	GLV harness routing and connector schedule	○ Backlog	ready	–	EV27-11, EV27-27	—	2026-10-10
EV27-7	Precharge / discharge circuit sizing	● Review	ready	–	EV27-10, EV27-101	Aidan	2026-09-22
EV27-8	BMS vendor selection and evaluation	● Review	ready	–	EV27-9	Aidan	2026-09-20
EV27-34	DL1 CLUB configuration and CAN map	🕒 In Progress	ready	–	EV27-35, EV27-36, EV27-37	Aidan	2026-09-26
EV27-14	Cell selection: Molicel P45B vs VTC6	● Review	ready	–	EV27-9, EV27-15, EV27-16, EV27-19	Aidan	2026-09-19
EV27-20	EMRAX 228 MV cooling loop layout	⊗ Blocked	ready	–	–	—	2026-10-24
EV27-28	Firewall design and material selection	🕒 In Progress	ready	–	–	—	2026-10-17
EV27-31	Mass budget vs 190 lb driver	🕒 In Progress	ready	–	EV27-33	Aidan	2026-09-26
EV27-32	Steering angle sensor equations	○ Ready	ready	–	EV27-37	—	2026-10-17

Electrical

13 work items · 5 blocked · arrows read left to right: a box must finish before the boxes it points to can start

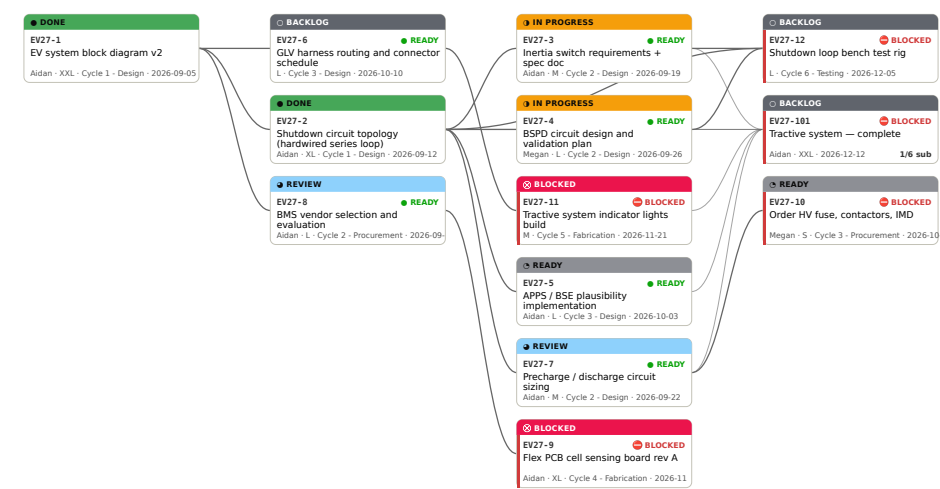


ID	WORK ITEM	STATE	NOW	WAITING ON	BLOCKS	OWNER	TAR
EV27-1	EV system block diagram v2	● Done	—	—	EV27-2, EV27-6, EV27-8, EV27-28, EV27-34	Aidan	2021
EV27-2	Shutdown circuit topology (hardwired series loop)	● Done	—	—	EV27-3, EV27-4, EV27-5, EV27-7, EV27-12, EV27-36, EV27-101	Aidan	2021
EV27-6	GLV harness routing and connector schedule	○ Backlog	ready	—	EV27-11, EV27-27	—	2021
EV27-8	BMS vendor selection and evaluation	● Review	ready	—	EV27-9	Aidan	2021
EV27-11	Tractive system indicator lights build	⊗ Blocked	blocked	EV27-6	EV27-101	—	2021
EV27-3	Inertia switch requirements + spec doc	🕒 In Progress	ready	—	EV27-12, EV27-101	Aidan	2021
EV27-4	BSPD circuit design and validation plan	🕒 In Progress	ready	—	EV27-12, EV27-101	Megan	2021
EV27-5	APPS / BSE plausibility implementation	🕒 Ready	ready	—	EV27-101	Aidan	2021
EV27-7	Precharge / discharge circuit sizing	● Review	ready	—	EV27-10, EV27-101	Aidan	2021
EV27-9	Flex PCB cell sensing board rev A	⊗ Blocked	blocked	EV27-8, EV27-14	EV27-21	Aidan	2021
EV27-10	Order HV fuse, contactors, IMD	🕒 Ready	blocked	EV27-7	—	Megan	2021
EV27-101	Tractive system — complete	○ Backlog	blocked	EV27-3, EV27-4, EV27-5, EV27-7, EV27-11	—	Aidan	2021
EV27-12	Shutdown loop bench test rig	○ Backlog	blocked	EV27-3, EV27-4	EV27-38	—	2021

10 work items · 7 blocked · arrows read left to right: a box must finish before the boxes it points to can start

Drivetrain

4 work items · 1 blocked · arrows read left to right: a box must finish before the boxes it points to can start

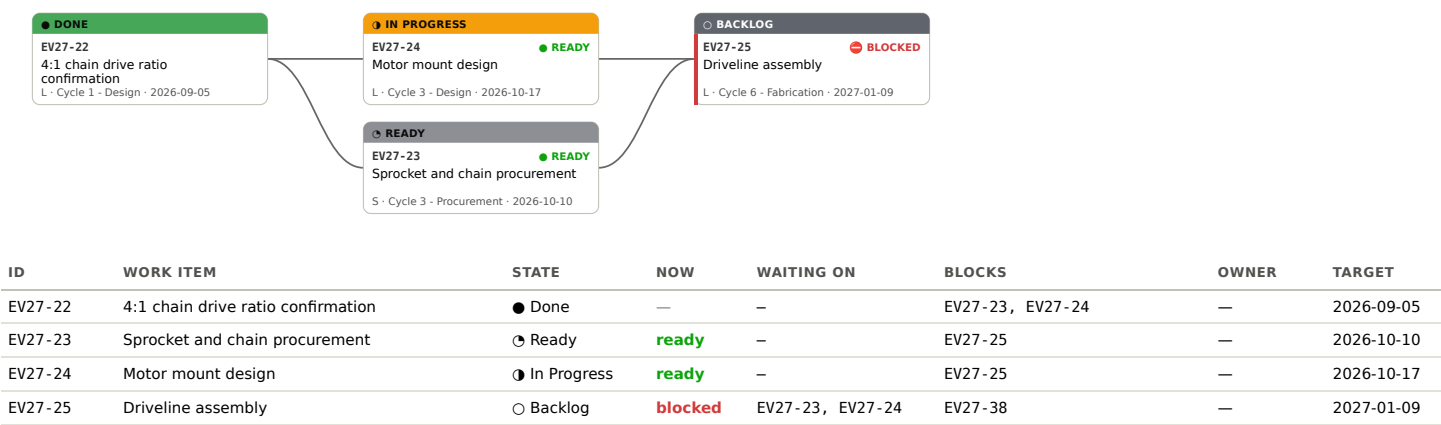

Structural & Aero

4 work items · 2 blocked · arrows read left to right: a box must finish before the boxes it points to can start

○ BACKLOG

EV27-26

Accumulator mounting structure

XL · Cycle 4 - Design · 2026-11-07

⛔

BLOCKED

× DROPPED

EV27-29

Impact attenuator test article

M · Cycle 4 - Testing · 2026-11-14

🕒 IN PROGRESS

EV27-28

Firewall design and material selection

M · Cycle 3 - Design · 2026-10-17

●

READY

🕒 READY

EV27-27

Chassis nodes for HV routing

M · Cycle 3 - Design · 2026-10-24


⛔

BLOCKED

ID	WORK ITEM	STATE	NOW	WAITING ON	BLOCKS	OWNER	TARGET
EV27-29	Impact attenuator test article	× Dropped	—	—	—	—	2026-11-14
EV27-28	Firewall design and material selection	🕒 In Progress	ready	—	—	—	2026-10-17
EV27-27	Chassis nodes for HV routing	🕒 Ready	blocked	EV27-6	—	—	2026-10-24
EV27-26	Accumulator mounting structure	○ Backlog	blocked	EV27-15	—	—	2026-11-07


Vehicle Dynamics

4 work items · 1 blocked · arrows read left to right: a box must finish before the boxes it points to can start

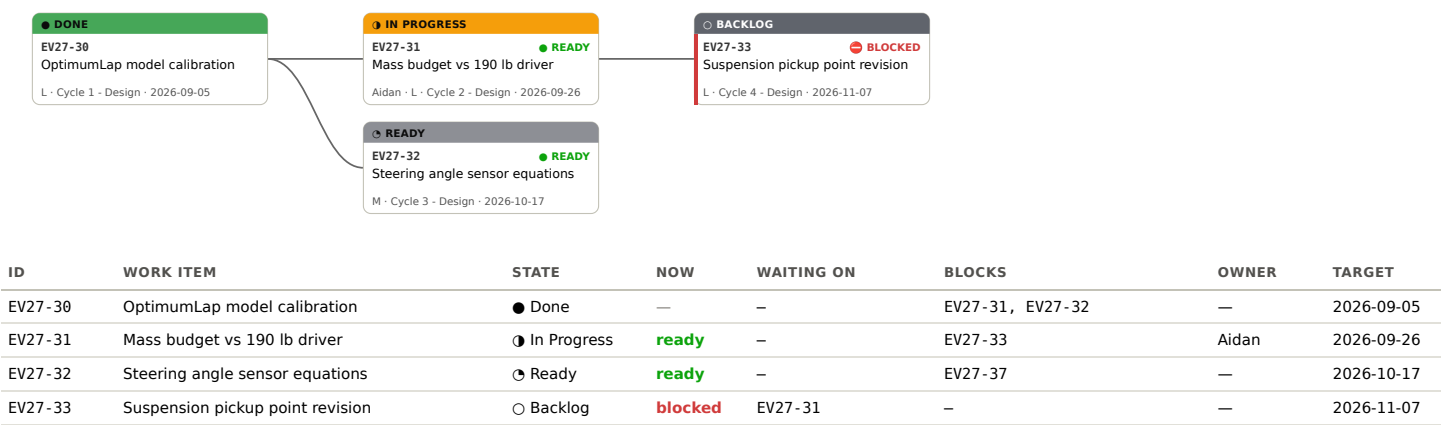

Integration & DAQ

5 work items · 4 blocked · arrows read left to right: a box must finish before the boxes it points to can start

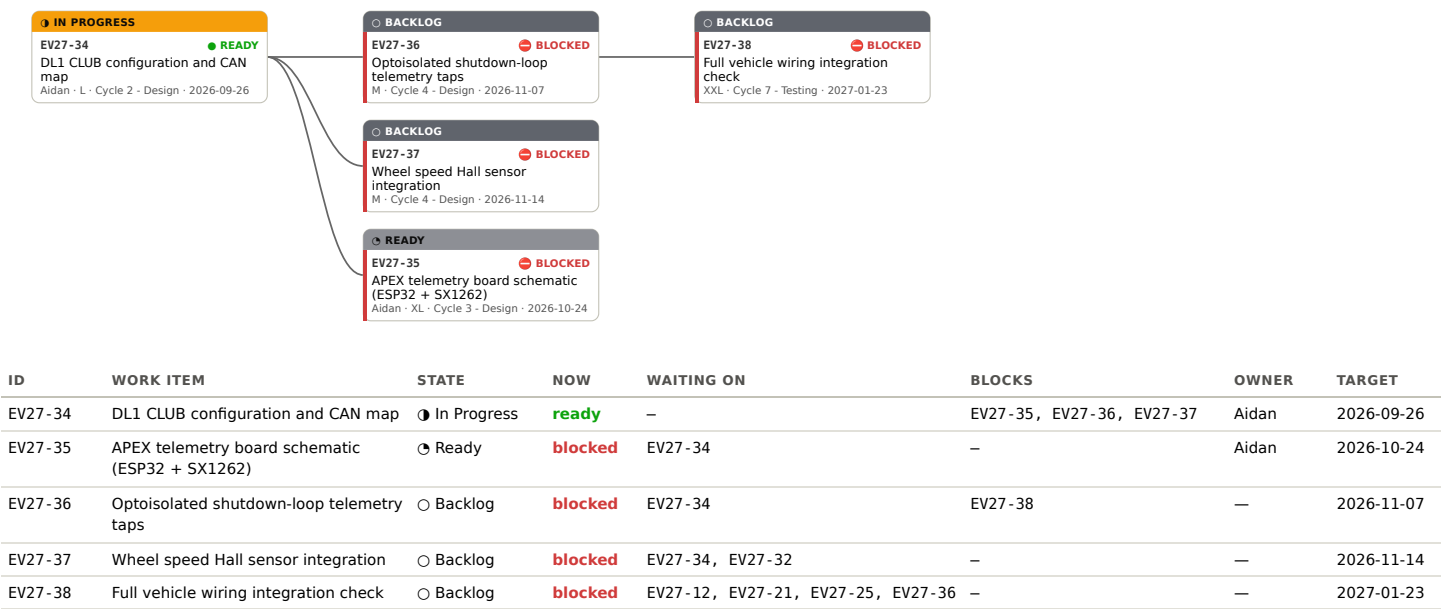

Schedule conflicts

The blocker is due *after* the thing waiting on it. Both dates cannot hold; one of them is wrong.

BLOCKER		DUE	BLOCKS		DUE
EV27-19	Purchase order: Enepaq modules	2027-02-01	EV27-21	Accumulator assembly and pack build	2026-12-19
EV27-19	Purchase order: Enepaq modules	2027-02-01	EV27-100	Accumulator — complete	2026-12-31

Cross-module dependencies

Where one lead is waiting on another. These are the ones that slip.

BLOCKER	OWNED BY	BLOCKS	OWNED BY	BLOCKER STATE
EV27 - 14	Powertrain	EV27 - 9	Electrical	Review
EV27 - 9	Electrical	EV27 - 21	Powertrain	Blocked
EV27 - 13	Powertrain	EV27 - 22	Drivetrain	Done
EV27 - 15	Powertrain	EV27 - 26	Structural & Aero	In Progress
EV27 - 6	Electrical	EV27 - 27	Structural & Aero	Backlog
EV27 - 1	Electrical	EV27 - 28	Structural & Aero	Done
EV27 - 13	Powertrain	EV27 - 31	Vehicle Dynamics	Done
EV27 - 1	Electrical	EV27 - 34	Integration & DAQ	Done
EV27 - 2	Electrical	EV27 - 36	Integration & DAQ	Done
EV27 - 32	Vehicle Dynamics	EV27 - 37	Integration & DAQ	Ready
EV27 - 12	Electrical	EV27 - 38	Integration & DAQ	Backlog
EV27 - 21	Powertrain	EV27 - 38	Integration & DAQ	Backlog
EV27 - 25	Drivetrain	EV27 - 38	Integration & DAQ	Backlog
